



## WORKS NOTIFICATION

### CONSTRUCTION UPDATE KENSINGTON

**20 AUGUST – 31 AUGUST 2018**

This notification provides additional information about upcoming works in Kensington during the month of August.

#### Driveway construction update

Further to the August 2018 Construction Update, additional concreting works are required to complete the high voltage transmission tower maintenance driveway off Kensington Road.

##### What we are doing

- Concreting a section of the maintenance driveway
- Using a small excavator and saw cutter to break-up concrete. Concrete will be re-laid to finalise construction.

##### When

- 7am – 6pm, Monday 20 to Wednesday 22 August.

##### What to be aware of

- These works are expected to generate intermittent periods of medium level noise
- The works will require the closure of a single northbound lane on Kensington Road, between Hobsons Road and the rail bridge
- A shuttle flow arrangement will be in place to safely direct traffic, pedestrians and cyclists around the work area
- Access to private properties and business will be maintained at all times.

#### Service investigations

Further site investigations will be undertaken on Childers Street and within the rail corridor to identify and confirm the location of existing underground services and help inform detailed planning for construction of the western tunnel entrance.

##### What we are doing

- Removing vegetation (callistemon hedge) along the rail embankment on Childers Street to make room for NDD and geotechnical investigations. Removal of this vegetation is also required for the future construction of the western tunnel entrance
- Non-destructive digging (NDD) which involves using a vacuum truck to excavate carefully into the ground to find, inspect and survey the services
- Backfilling and reinstating the multiple test sites.


##### When

- 7am – 6pm, Monday 27 to Friday 31 August.

##### What to be aware of

- Work crews will occupy each test site within the works area for a short period and works will be staged throughout the day to minimise disruption to traffic, pedestrians and on-street parking
- Up to five on-street parking bays along Childers Street will be progressively closed to maintain traffic flow
- Traffic controllers will be in place throughout the works to direct traffic and pedestrians safely around the work site and to provide access to the rail corridor via Kensington Road

- Clearing of vegetation along the rail corridor embankment is required to establish an access path for service investigations. This activity will involve the use of landscaping equipment such as, mulchers and small excavators
- The area will be inspected for the presence of wildlife prior to any works. Any identified fauna will be safely relocated by qualified wildlife handlers
- These works are expected to generate intermittent periods of high level noise during NDD and vegetation clearing activities. We will take measures to minimise noise from our works wherever possible.

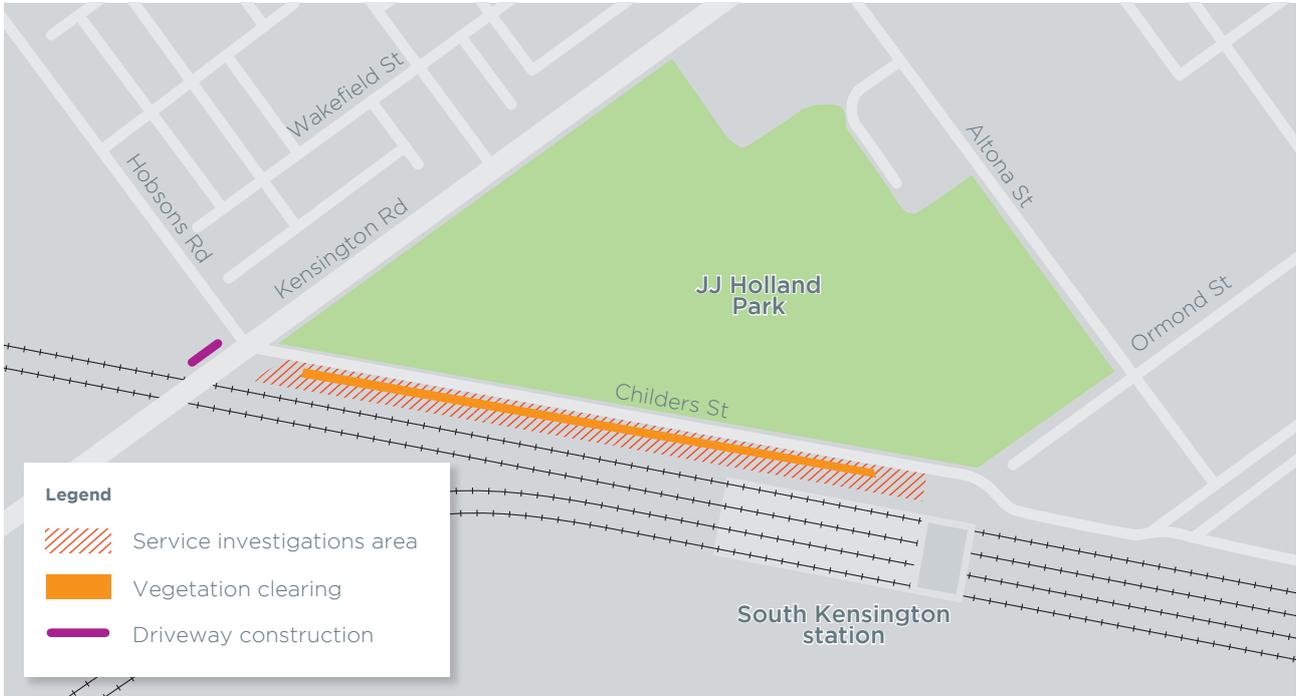

### More information

To find out more about the Metro Tunnel Project and register for future email updates:

-  [metrotunnel.vic.gov.au](http://metrotunnel.vic.gov.au)
-  1800 105 105 (24 hours a day, 7 days a week)  
Press 2 and follow the prompts
-  [facebook.com/metrotunnel](https://facebook.com/metrotunnel)
-  Subscribe to eNews or construction notification emails: [metrotunnel.vic.gov.au/subscribe](mailto:metrotunnel.vic.gov.au/subscribe)



**Interpreter Service**  
**(03) 9280 0700**

Arabic	العربية	Russian	Русский
Cantonese	廣東話	Serbian	Српски
Greek	Ελληνικά	Sinhalese	සිංහල
Italian	Italiano	Spanish	Español
Korean	한국어	Turkish	Türkçe
Macedonian	Македонски	Vietnamese	Tiếng Việt
Mandarin	普通话		

It should be noted that this information is current at the time of printing, however due to unforeseen circumstances, changes may occur. Please visit [metrotunnel.vic.gov.au](http://metrotunnel.vic.gov.au) for the latest updates.
